



CONSTRUCTION OF TWO STORY BUILDING ISLAMABAD

**01-Jan-18
to
10-Aug-18**

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Total Float	2018											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Construction of two story Building in Islamabad		190	01-Jan-18	10-Aug-18	0	10-Aug-18, Construction of two story Building											
Preliminary Works		190	01-Jan-18	10-Aug-18	0	10-Aug-18, Preliminary Works											
1PSM	Start of Project	0	01-Jan-18		0	Start of Project, 01-Jan-18											
PLO1	Contract Agreement	1	01-Jan-18	01-Jan-18	0	Contract Agreement											
PLO2	Issuance of Drawing	1	02-Jan-18	02-Jan-18	0	Issuance of Drawing											
PLO3	Issuance of NOC	1	03-Jan-18	03-Jan-18	0	Issuance of NOC											
PLO4	Mobalization	7	04-Jan-18	11-Jan-18	0	Mobalization											
PLO5	Initial Survey	1	12-Jan-18	12-Jan-18	0	Initial Survey											
PLO6	Site Clearence	1	13-Jan-18	13-Jan-18	0	Site Clearence											
zPEM	Finish Project.	0		10-Aug-18	0	Finish Project., 10-Aug-18											
Construction work		177	13-Jan-18	08-Aug-18	2	08-Aug-18, Construction work:											
Foundation work		54	13-Jan-18	16-Mar-18	125	16-Mar-18, Foundation work											
Earthwork		54	13-Jan-18	16-Mar-18	125	16-Mar-18, Earthwork											
1FESM	Start of Earth wok	0	13-Jan-18		0	Start of Earth wok, 13-Jan-18											
FEO1	Excavation Layout	1	13-Jan-18	13-Jan-18	0	Excavation Layout											
FEO2	Excavation	3	15-Jan-18	17-Jan-18	0	Excavation											
FEO3	Termite Proofing at Excavation Level	1	18-Jan-18	18-Jan-18	0	Termite Proofing at Excavation Level											
FEO4	First Backfilling Layer with compaction.	2	07-Mar-18	08-Mar-18	0	First Backfilling Layer with compaction.											
FEO5	Termite Proofing after 1st Backfilling	1	09-Mar-18	09-Mar-18	0	Termite Proofing after 1st Backfilling											
FEO6	2nd Backfilling Layer with Compaction.	2	10-Mar-18	12-Mar-18	0	2nd Backfilling Layer with Compaction.											
FEO7	Termite Proofing after 2st Backfilling	1	13-Mar-18	13-Mar-18	0	Termite Proofing after 2st Backfilling											
FEO8	Last Backfilling layer with Compaction.	2	14-Mar-18	15-Mar-18	0	Last Backfilling layer with Compaction.											
FEO9	Termite Proofing after Last Backfilling Layer.	1	16-Mar-18	16-Mar-18	0	Termite Proofing after Last Backfilling Layer.											
FEFM	Finish of Earth work	0		16-Mar-18	125	Finish of Earth work, 16-Mar-18											
Structure Work		43	19-Jan-18	09-Mar-18	131	09-Mar-18, Structure Work											
1FSSM	Start of Foundation Structure work	0	19-Jan-18		0	Start of Foundation Structure work, 19-Jan-18											
FS001	Layout for PCC.	1	19-Jan-18	19-Jan-18	0	Layout for PCC.											
FS002	PCC for Columns Foundation	3	20-Jan-18	23-Jan-18	0	PCC for Columns Foundation											
FS003	PCC for wall Foundations	3	20-Jan-18	23-Jan-18	15	PCC for wall Foundations											
FS004	Reinforcement Fixing of Columns footings	6	24-Jan-18	30-Jan-18	0	Reinforcement Fixing of Columns footings											
FS005	Formwork of Columns Footing..	7	31-Jan-18	07-Feb-18	0	Formwork of Columns Footing..											
FS006	Concrete pouring Columns Footings	1	08-Feb-18	08-Feb-18	0	Concrete pouring Columns Footings											
FS007	Reinforcement Fixing of Columns Upto plinth.	6	09-Feb-18	15-Feb-18	0	Reinforcement Fixing of Columns Upto plinth.											
FS008	Formwork of Columns upto Plinth.	5	16-Feb-18	21-Feb-18	0	Formwork of Columns upto Plinth.											
FS009	Concrete Pouring in Columns.	1	22-Feb-18	22-Feb-18	0	Concrete Pouring in Columns.											
FS010	Brikcwork in wall Foundations.	5	24-Jan-18	29-Jan-18	15	Brikcwork in wall Foundations.											
FS011	Brikcwork of Walls upto plinth.	6	30-Jan-18	05-Feb-18	15	Brikcwork of Walls upto plinth.											
FS012	Reinforcement Fixing in Plinth Beams.	5	23-Feb-18	28-Feb-18	0	Reinforcement Fixing in Plinth Beams.											
FS013	Formwork of Plinth beams.	4	01-Mar-18	05-Mar-18	0	Formwork of Plinth beams.											
FS014	Concrete pouring in Plinth Beams.	1	06-Mar-18	06-Mar-18	0	Concrete pouring in Plinth Beams.											
FS015	Horizatntal DPC.	3	07-Mar-18	09-Mar-18	0	Horizatntal DPC.											
FS016	Construction of Septic Tank	15	17-Feb-18	06-Mar-18	134	Construction of Septic Tank											
FS017	Vertical DPC.	3	03-Mar-18	06-Mar-18	0	Vertical DPC.											
FSFM	Finsh of Foundation Structure Work.	0		06-Mar-18	134	Finsh of Foundation Structure Work., 06-Mar-18											
Ground Floor		50	17-Mar-18	15-May-18	75	15-May-18, Ground Floor											
GFO1SM	Start of Ground Floor Construction work.	0	17-Mar-18		0	Start of Ground Floor Construction work., 17-Mar-18											
GFFM	Finish of Ground Floor Construction work.	0		04-May-18	84	Finish of Ground Floor Construction work., 04-May-18											
Structure		43	17-Mar-18	07-Mau-18	82	07-May-18, Structure											
1GFSSM	Start of structure work at Ground Floor.	0	17-Mar-18		0	Start of structure work at Ground Floor., 17-Mar-18											
GFSS001	Floor Concreting.	1	17-Mar-18	17-Mar-18	0	Floor Concreting.											

█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ⇨ summary






CONSTRUCTION OF TWO STORY BUILDING ISLAMABAD

**01-Jan-18
to
10-Aug-18**

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Total Float	2018													
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
GFSSM	Finish of Structure work at Ground Floor	0		07-May-18	82														
Architecture		30	10-Apr-18	15-May-18	75														
1GFASM	Start of Architecture work.	0	10-Apr-18		75														
QFA001	Plastering work.	4	10-Apr-18	13-Apr-18	75														
QFA002	Wall tiles fixing in Kitchen and Baths	3	14-Apr-18	17-Apr-18	84														
QFA003	False Ceiling Work.	18	14-Apr-18	05-May-18	75														
QFA004	Floor tile in rooms.	8	27-May-18	15-May-18	75														
QFA005	Floor tile in Toilets & kitchens	4	24-Apr-18	27-Apr-18	84														
QFA006	Paint work at Ground floor.	16	26-Apr-18	15-May-18	75														
QFA007	Installation of Kitchen Units and Fixing Staircase Railing	5	28-Apr-18	04-May-18	84														
QFA008	Doors, Windows and Ventilaters Installation.	5	10-May-18	15-May-18	75														
QFAFM	Finish of Architecture work.	0		15-May-18	75														
Electrical		29	10-Apr-18	14-May-18	76														
1GFESM	Start of Electrical work.	0	10-Apr-18		105														
QFEO01	Slab Conduiting for Electrical wiring.	1	25-May-18	05-May-18	83														
QFEO02	Electrical Conduiting in walls.	3	10-Apr-18	12-Apr-18	85														
QFEO03	Electrical boards, switches, sockets etc Fixing.	5	27-May-18	12-May-18	76														
QFEO04	Fan and Lightning items installation.	5	29-May-18	14-May-18	76														
QFEFM	Finishing of Electrical work.	0		14-May-18	76														
Plumbing		14	18-Apr-18	04-May-18	84														
1GFPSM	Start Of Plumbing work.	0	18-Apr-18		84														
QFPO01	Pipes fittings in Toilets & Kitchens.	4	18-Apr-18	21-Apr-18	84														
QFPO02	Sanitary wares installation.	4	28-Apr-18	03-May-18	84														
QFPO03	Taps and Showers Installations.	1	24-May-18	04-May-18	84														
QFPFM	Finish of Plumbing work.	0		04-May-18	84														
Waterproofing		1	23-Apr-18	23-Apr-18	84														
QFW	Bitumen Painting under Floor tiles in Kitchen & Baths.	1	23-Apr-18	23-Apr-18	84														
First Floor		80	28-May-18	08-Aug-18	2														
Structure		42	28-May-18	25-Jun-18	40														
1FFSSM	Start of structure work at First Floor.	0	28-May-18		0														
FFS001	Surveying and layout for column positions.	1	28-May-18	08-May-18	0														
FFS002	Reinforcement fixing of Columns.	7	29-May-18	16-May-18	0														
FFS003	Brickwork of walls.	11	17-May-18	29-May-18	0														
FFS004	Formwork of Columns and staircase.	7	30-May-18	06-Jun-18	0														
FFS005	Concrete pouring in Columns and staircase.	1	07-Jun-18	07-Jun-18	0														
FFS006	Reinforcement fixing of Staircase	2	01-Jun-18	02-Jun-18	3														
FFS007	Formwork of slab.	8	08-Jun-18	16-Jun-18	0														
FFS008	Reinforcement fixing of slab beams and slab.	6	18-Jun-18	23-Jun-18	12														
FFS009	Concrete Pouring of Slab.	1	25-Jun-18	25-Jun-18	12														
FFFSM	Finish of Structure work at First Floor	0		25-Jun-18	40														
Architecture		45	18-Jun-18	08-Aug-18	2														
1FFASM	Start of Architecture work.	0	18-Jun-18		0														

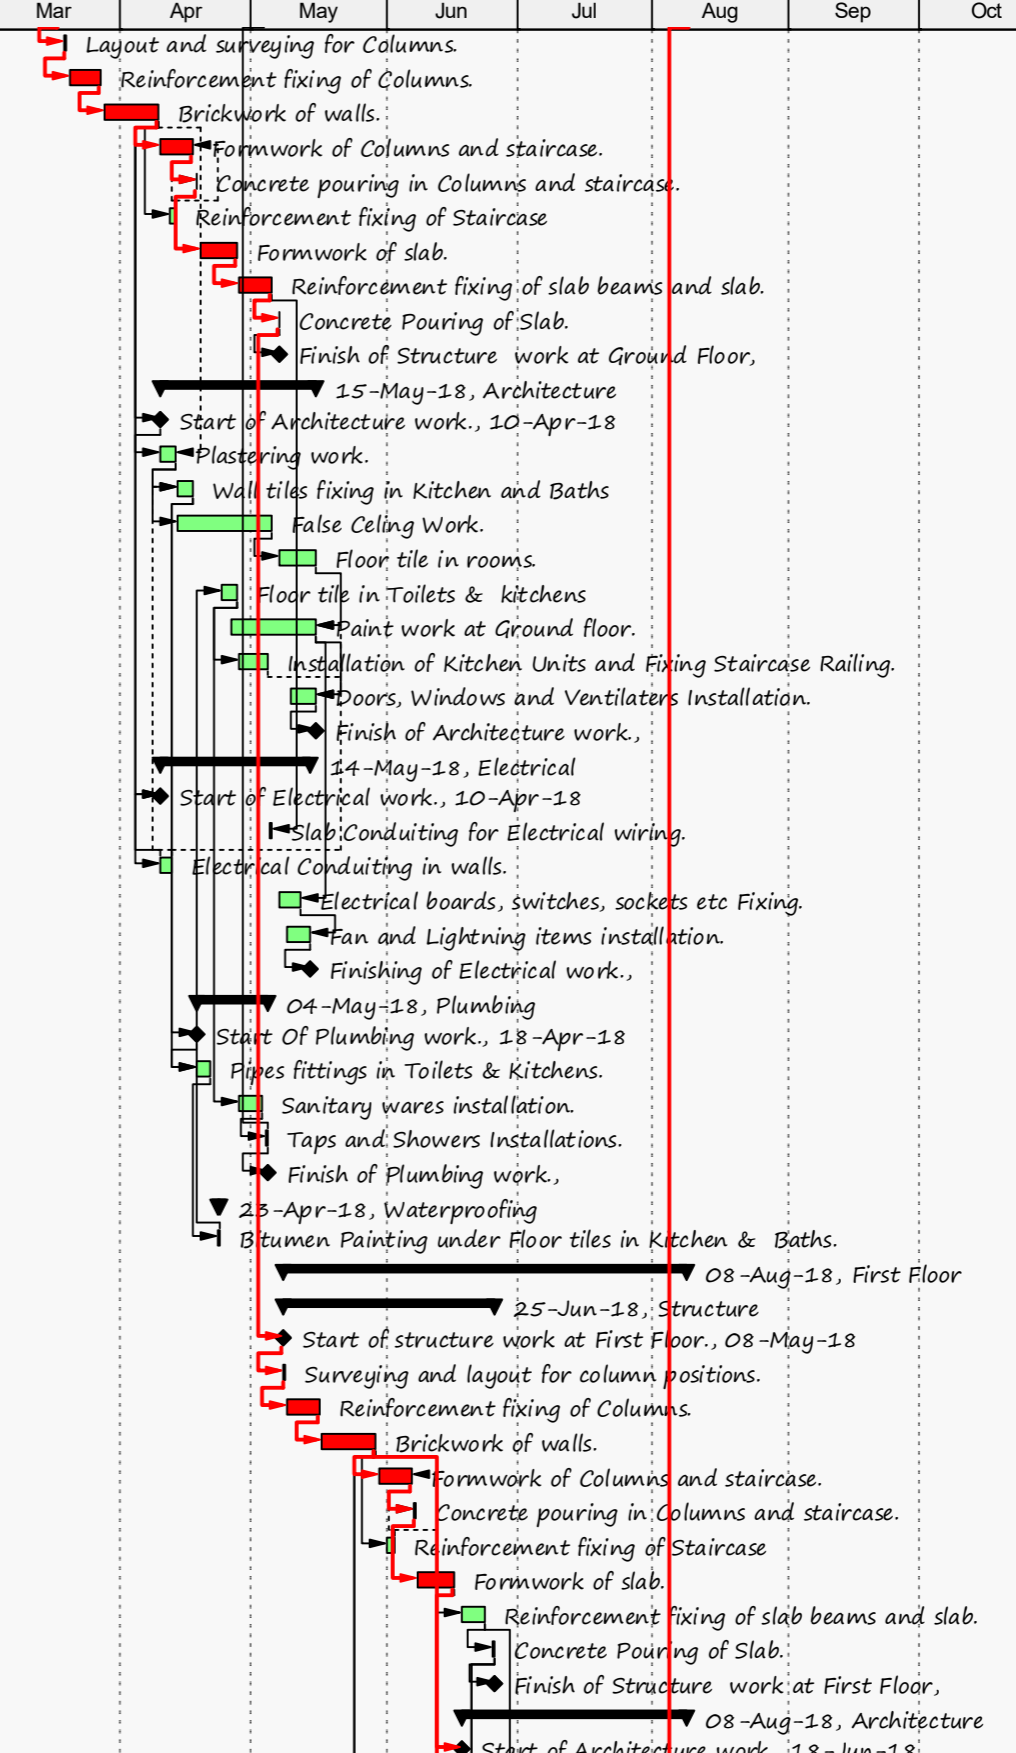

█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ⇨ summary

PE: Engr. TASAWAR ALI






CONSTRUCTION OF TWO STORY BUILDING ISLAMABAD

**01-Jan-18
to
10-Aug-18**

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Total Float	2018														
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec			
FFA001	Plastering work.	4	18-Jun-18	21-Jun-18	0															
FFA002	False Ceiling Work.	18	22-Jun-18	12-Jul-18	0															
FFA003	Wall tiles fixing in Baths	3	22-Jun-18	25-Jun-18	15															
FFA004	Floor tile in rooms.	8	13-Jul-18	21-Jul-18	0															
FFA005	Floor tile in Toilets	3	02-Jul-18	04-Jul-18	20															
FFA006	Paint work at First Floor.	15	23-Jul-18	08-Aug-18	0															
FFA007	Fixing Staircase Railing.	5	05-Jul-18	10-Jul-18	20															
FFA008	Doors, Windows and Ventilaters Installation.	5	03-Aug-18	08-Aug-18	0															
FFAFM	Finish of Architecture work.	0		08-Aug-18	2															
Electrical		27	30-May-18	29-Jun-18	36															
1FFESM	Start of Electrical work.	0	30-May-18		63															
FFE001	Slab Conduiting for Electrical wiring.	1	23-Jun-18	23-Jun-18	41															
FFE002	Electrical Conduiting in walls.	3	30-May-18	01-Jun-18	13															
FFE003	Electrical boards, switches, sockets etc Fixing.	5	22-Jun-18	27-Jun-18	36															
FFE004	Fans and Lightning Items Installation	5	25-Jun-18	29-Jun-18	36															
FFEFM	Finishing of Electrical work.	0		29-Jun-18	36															
Plumbing		14	26-Jun-18	11-Jul-18	26															
1FFPSM	Start Of Plumbing work.	0	26-Jun-18		20															
FFP001	Pipes fittings in Toilets & Kitchens.	4	26-Jun-18	29-Jun-18	20															
FFP002	Sanitary wares installation.	4	06-Jul-18	10-Jul-18	26															
FFP003	Taps and Showers Installations.	1	11-Jul-18	11-Jul-18	26															
FFPFM	Finish of Plumbing work.	0		11-Jul-18	26															
Waterproofing		1	30-Jun-18	30-Jun-18	20															
FFW	Bitumen Painting Under Floor tiles in Toilets	1	30-Jun-18	30-Jun-18	20															
Roof		28	26-Jun-18	27-Jul-18	12															
Structure		20	26-Jun-18	18-Jul-18	20															
1RFSSM	Start of structure of at Roof Floor.	0	26-Jun-18		12															
RFS001	surveying and layout for column positions.	1	26-Jun-18	26-Jun-18	12															
RFS002	Reinforcement fixing of Columns.	1	27-Jun-18	27-Jun-18	12															
RFS003	Brickwork of walls	2	28-Jun-18	29-Jun-18	12															
RFS004	Formwork of Columns.	1	30-Jun-18	30-Jun-18	12															
RFS005	Concrete pouring in Columns.	1	02-Jul-18	02-Jul-18	12															
RFS006	Formwork of slab.	2	03-Jul-18	04-Jul-18	12															
RFS007	Reinforcement fixing of slab beams and slab.	3	05-Jul-18	07-Jul-18	12															
RFS008	Concrete Pouring of Slab.	1	09-Jul-18	09-Jul-18	12															
RFS009	Construction of Parapet wall	8	10-Jul-18	18-Jul-18	12															
RFSFM	Finish of Structure work at Roof Floor.	0		18-Jul-18	20															
Architecture		24	30-Jun-18	27-Jul-18	12															
1RFASM	Start of Architecture work.	0	30-Jun-18		28															
RFA001	Plastering work.	1	19-Jul-18	19-Jul-18	12															
RFA002	False Ceiling Work.	3	20-Jul-18	23-Jul-18	12															
RFA003	Floor tile fixing at Mumty floor	1	24-Jul-18	24-Jul-18	12															
RFA004	Paint work.	2	25-Jul-18	26-Jul-18	12															
RFA005	Doors and Windows Installation.	1	27-Jul-18	27-Jul-18	12															
RFAFM	Finish of Architecture work.	0		27-Jul-18	12															
Electrical		18	30-Jun-18	20-Jul-18	18															
1RFESM	Start of Electrical work.	0	30-Jun-18		36															
RFE001	Slab Conduiting for Electrical wiring.	1	07-Jul-18	07-Jul-18	29															
RFE002	Electrical Conduiting in walls.	1	30-Jun-18	30-Jun-18	28															
RFE003	Electrical boards, switches, sockets etc Fixing.	1	20-Jul-18	20-Jul-18	18															
RFE004	Lightning Items installation.	2	19-Jul-18	20-Jul-18	18															

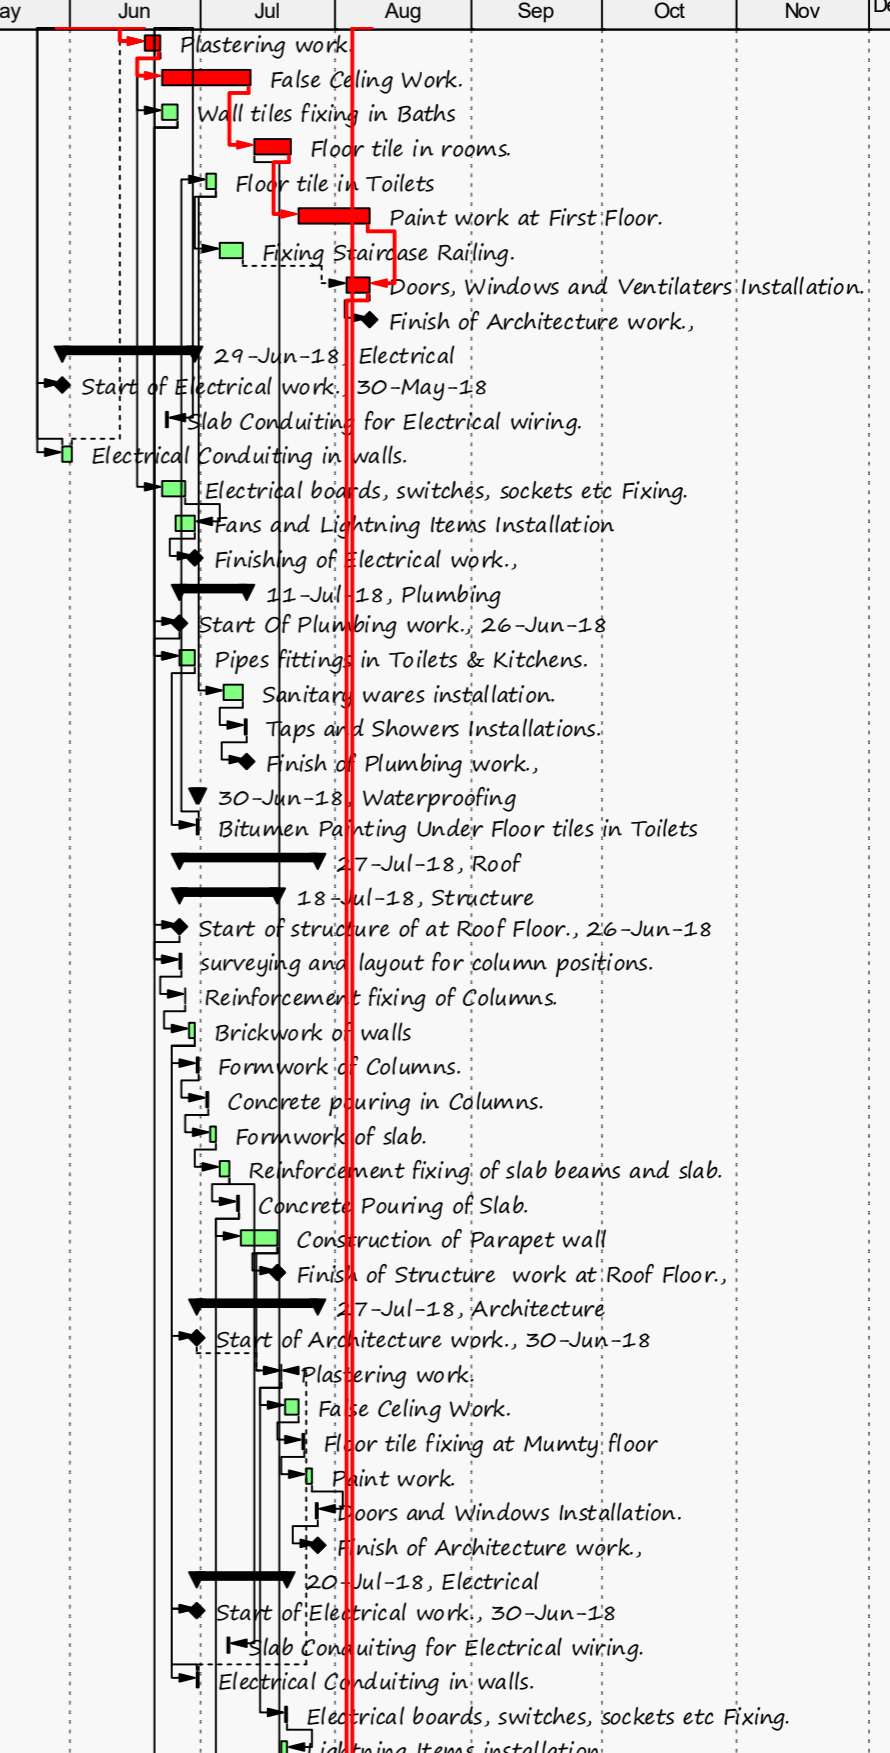

█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ⇐ summary

PE: Engr. TASAWAR ALI






CONSTRUCTION OF TWO STORY BUILDING ISLAMABAD

**01-Jan-18
to
10-Aug-18**

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Total Float	2018														
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec			
RFEFM	Finishing of Electrical work.	0		20-Jul-18	18															
Waterproofing		6	10-Jul-18	16-Jul-18	22															
RFW	Water proofing work over terrace floor and Mumty ro.	6	10-Jul-18	16-Jul-18	22															
External Finishes		33	26-Jun-18	02-Aug-18	7															
1EXTSM	Start of External Finishes.	0	26-Jun-18		15															
EXT001PL	External Plastering	7	05-Jul-18	13-Jul-18	7															
EXT002PT	External Paint work	12	13-Jul-18	26-Jul-18	7															
EXT003TF	Tuff Tile Fixng outside for parking.	6	27-Jul-18	02-Aug-18	7															
EXTFM	End of External Finishes.	0		02-Aug-18	7															
Closing		2	09-Aug-18	10-Aug-18	0															
CLO1	Final Meeting with Consultant.	1	09-Aug-18	09-Aug-18	0															
CLO2	Final Meeting with Client and Hand over building.	1	10-Aug-18	10-Aug-18	0															

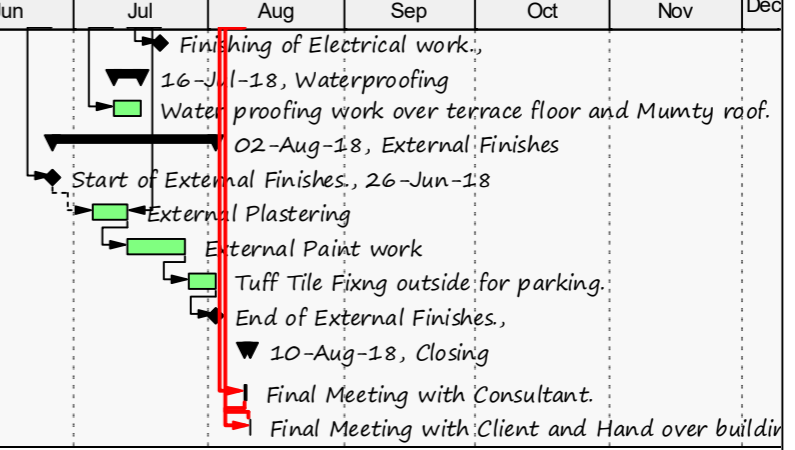

█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ⇨ summary

PE: Engr. TASAWAR ALI
